



TECHNICAL PROPOSAL

Design, Development, Deployment and Maintenance of the Multilingual Website & Admin CMS Portal

Client: CSIR Innovation Complex, Mumbai

Council of Scientific & Industrial Research, Ministry of Science & Technology, Government of India

Trilingual (English / Hindi / Marathi) · 24 Incubation Labs · GIGW 3.0 & CQW certified

Submitted By



SOURCE SOFT SOLUTIONS PRIVATE LIMITED

B-21, CESPL Building, Sector 67, Noida, Gautam Buddha Nagar, Uttar Pradesh – 201301

info@sourcesoftsolutions.com · +91 98999 41672 · www.sourcesoftsolutions.com

Submitted in response to the Scope of Work for the website of CSIR Innovation Complex, Mumbai



Table of Contents

Technical proposal for the institutional website, admin CMS portal and annual maintenance.

·	About the Company	Company profile, capabilities and leadership
01	Executive Summary	The proposal in one page, with engagement facts
02	Our Understanding of the Requirement	Audiences, journeys, scope boundaries
03	Project Objectives	Six outcomes we will be measured against
04	Requirement to Solution Compliance Matrix	Every SOW clause mapped to a deliverable
05	Information Architecture	Sitemap, page structure and content types
06	Solution & Technology Architecture	Edge, application, CMS, data and hosting layers
07	Data Flow Diagrams	Context level plus enquiry and publishing flows
08	Public Website — Modules & Features	Every page named in the Scope of Work
09	The 24 Incubation Labs Module	Fields, statuses and the discovery-to-enquiry path
10	Admin CMS Portal	Modules, settings and roles
11	Enquiry, Email & Anti-Spam	Four forms, SendGrid/Resend, Cloudflare Turnstile
12	Security, Hosting & Compliance	MeitY hosting, Cloudflare, IAAP, CQW, cybersecurity audit
13	Multilingual, SEO & Performance	Three languages, discoverability and speed targets
14	UI Design Concepts & Mock Screens	Three public-site variants plus the admin CMS
15	Implementation Methodology & Timeline	Five phases with approval and audit gates
16	Annual Maintenance & Support	Monitoring, content support, social media handling
17	Deliverables, Assumptions & Clarifications	What CICM owns, and what we need confirmed

How to read this proposal

Section 04 is the compliance record — every requirement in the Scope of Work with our response. Sections 06–07 carry the architecture and data-flow diagrams; Section 14 carries three UI design variants for the public website plus the admin CMS.

About the Company

Who we are, what we deliver, and the leadership accountable for this engagement.

We at Source Soft Solutions provide AI, cloud, and data solutions to drive innovation and growth across industries. Our services focus on data modernization, analytics, and cloud infrastructure management, helping businesses unlock new possibilities with AI/ML, data insights, and scalable cloud technologies.

Empowering organizations to thrive in the digital landscape.

Headquartered in Edison, New Jersey, with an office in Dubai and our primary engineering centre in Noida, India, we run long-term maintenance and support contracts on the same platforms we engineer.

What we deliver

Transformative Data Solutions	Robust Cloud Services
Advanced AI Capabilities	Insightful Analytics
Seamless Integration	Custom Software Development
Data Security & Compliance	Training & Support

Leadership team



Alok Dharayan · President

25+ years delivering engineering solutions to complex global problems. Masters, New Jersey Institute of Technology. Sets delivery governance and client accountability across Source Soft Solutions' enterprise and government engagements.



Vijay Konar · Chief Technology Officer

Leads all product and platform engineering at Source Soft Solutions. Deep expertise in full-stack development, AWS cloud architecture and data engineering; owns technical standards, release controls and architecture reviews.



Vikram Sharma · Solutions Lead

Architects client engagements end-to-end — from requirement study and solution design to transition-in and steady-state operations. Background in enterprise consulting and large-scale application maintenance programmes.

01 Executive Summary

What we are proposing, in one page.

CSIR Innovation Complex, Mumbai requires a professional, secure and fully manageable institutional website with a dedicated backend CMS, hosted on MeitY-approved infrastructure in India. We propose to design, develop, deploy and maintain a trilingual website in English, Hindi and Marathi, whose defining feature is a dedicated module promoting the **24 incubation labs** available to start-ups, MSMEs, industries, researchers and innovators — each lab with its own detail page, facilities, equipment list, brochure, live status and enquiry route.

We will deliver an accessible, GIGW 3.0-conformant institutional platform — CQW certified by STQC, cybersecurity audited by a CERT-In empanelled auditor and IAAP-audited for accessibility — with a purpose-built admin CMS, four enquiry workflows wired to SendGrid or Resend, Cloudflare protection with Turnstile, and a full year of monitored maintenance and social-media handling.

Institutional website, three languages

Home, About (Innovation, Incubation, SDP), News, Notices, Tenders, Recruitments, Events, Downloads, Gallery, Important Links and Contact — presented identically in English, Hindi and Marathi.

24 Incubation Labs module

Listing and detail pages driven from the CMS: lab name and number, category, description, images, facilities, equipment, suitability, brochure PDF, Available / Occupied / Coming Soon status, contact and enquiry button.

Login-protected admin CMS

Dashboard plus management of news, notices, tenders, recruitments, events, downloads, gallery, sliders, important links, labs, enquiries, website settings and email settings, with role-based access and PDF/image upload.

Secure, compliant, protected

MeitY-approved hosting in India, Cloudflare DNS/SSL/WAF/bot protection, Turnstile CAPTCHA on every public form, server hardening, backups, and the IAAP, CQW and cybersecurity certifications required by the SOW.

Annual maintenance & social media

Uptime, server, SSL, Cloudflare and backup monitoring; bug fixing; admin assistance and content uploads; monthly backup verification; and content creation, posting and live streaming across LinkedIn, X, Facebook, Instagram and YouTube.

Engagement at a glance

Deliverable	Trilingual public website + admin CMS portal + 24-lab module + enquiry workflows
Certifications in scope	IAAP accessibility audit, GIGW 3.0 / CQW from STQC, cybersecurity audit by a CERT-In / STQC empanelled auditor
Hosting	MeitY-approved data centre / cloud in India, fronted by Cloudflare
Email & anti-spam	SendGrid or Resend, configured from the admin panel; Cloudflare Turnstile on all public forms
Content	Provided by CICM; we implement, migrate, upload and maintain it



02 Our Understanding of the Requirement

A promotion platform for the incubation ecosystem, not just an information site.

Reading the Scope of Work, the website has two jobs at once. It must present CSIR Innovation Complex, Mumbai as an institution — innovation, incubation and the Skill Development Programme, with statutory content such as notices, tenders and recruitments — and it must actively convert interest into contact: a start-up, MSME, industry partner or researcher should be able to find a suitable lab, read its facilities and equipment, download its brochure and raise an enquiry that lands in the admin portal and in the right inbox within seconds.

Our governing principle: every public page ends in an action — read, download, or enquire — and every action is traceable in the admin portal.

Four audiences, four journeys

Start-ups	MSMEs & industry	Researchers	Public & applicants
Find an available lab → check facilities → download brochure → incubation enquiry / cohort application	Assess equipment and suitability → industry collaboration enquiry → follow-up from CICM	Browse labs by category → SDP and programme information → general contact enquiry	Notices, tenders, recruitments, events, gallery and downloads — in their own language

What is in scope — and what needs clarification

In our scope	Dependencies & clarifications
UI/UX design, trilingual frontend, admin CMS, 24-lab module, four enquiry workflows, email configuration, Turnstile, Cloudflare setup, hosting and deployment on MeitY-approved infrastructure, SSL, backups, server hardening, SEO and performance setup, certification support (IAAP, CQW/STQC, cybersecurity audit), training, documentation, one year of maintenance and social-media handling	Content, translations and social-media creative direction are provided by CICM. The payment-gateway item in the admin scope needs its business purpose confirmed (fees, event registration or cohort application charges) before we commit an integration; PG merchant onboarding, transaction charges, domain and cloud subscription costs, third-party licence fees and certification body charges are outside this technical scope.

03 Project Objectives

Six outcomes we will be measured against.

OBJECTIVE 01 A credible institutional presence Present the Complex — innovation, incubation and SDP — in a modern, responsive, accessible interface that works on any device and any connection.	OBJECTIVE 02 Promote the 24 labs Make every lab discoverable, comparable and enquirable, with live availability status and downloadable brochures.
OBJECTIVE 03 Independent content control Give CICM administrators a simple CMS that needs no developer for day-to-day notices, tenders, recruitments, events, gallery and lab updates.	OBJECTIVE 04 Trilingual parity English, Hindi and Marathi treated as equals in the CMS and on the frontend, with Unicode rendering and no font downloads.
OBJECTIVE 05 Certifiable compliance Build to GIGW 3.0 and WCAG from the first wireframe so IAAP, CQW and cybersecurity audits pass without redesign.	OBJECTIVE 06 Dependable operations Monitored uptime, verified backups, patched servers, and a named support route for the admin team through the maintenance term.



04 Requirement to Solution Compliance Matrix

Every clause of the Scope of Work, mapped to what we will build.

#	SOW clause	Requirement	Proposed solution	Status
1	2.1	IAAP certified accessibility audit as a pre-requisite	Accessibility engineered from wireframe stage; IAAP audit coordinated and findings remediated before go-live	Complied
2	2.1	GIGW 3.0 conformity via CQW certification from STQC	GIGW 3.0 checklist tracked through design and build; CQW submission and certification managed by us	Complied
3	2.1	Cybersecurity certification by a CERT-In / STQC empanelled auditor	Pre-audit hardening and internal testing, audit coordination, remediation and re-test	Complied
4	2.1	Hosting in a MeitY-approved data centre / cloud in India	Deployment to an approved provider with production environment, SSL, backups and hardening	Complied
5	2.1	Home page in English, Hindi and Marathi	Trilingual content model; language switch preserves page context; Unicode rendering	Complied
6	2.1	About CICM with Innovation, Incubation and SDP modules	Three dedicated sub-modules under About, each CMS managed	Complied
7	2.1	24 incubation labs highlight, listing page and detail pages	Dedicated labs module with home highlight, filterable listing and per-lab detail pages	Complied
8	2.1	News & Updates	CMS content type with listing, detail, attachments and archive	Complied
9	2.1	Notices / Announcements	Reference-numbered notices with publish/expiry dates and auto archival	Complied
10	2.1	Tenders	Tender listing with documents, corrigenda and closing dates	Complied
11	2.1	Recruitments / Careers	Advertisement listing with eligibility, last date and downloads	Complied
12	2.1	Events	Upcoming and past	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



#	SOW clause	Requirement	Proposed solution	Status
			events with venue, banner and gallery links	
13	2.1	Social media handles (LinkedIn, X, Facebook, Instagram, YouTube)	Linked site-wide, managed from website settings, plus handling under maintenance	Complied
14	2.1	Downloads	Categorised document repository with type, size and ordering	Complied
15	2.1	Gallery	Photo and video gallery grouped by event or theme with alt text	Complied
16	2.1	Important Links	CMS-managed external link module	Complied
17	2.1	Contact Us	Contact page with directory, map and general contact form	Complied
18	2.1	Start-up / MSME incubation enquiry form	Dedicated form with entity type, sector, stage and lab of interest	Complied
19	2.1	Industry collaboration enquiry form	Dedicated form capturing collaboration area, facility needed and timeline	Complied
20	2.1	General contact form	Contact form routed to the admin portal and notification inbox	Complied
21	2.1	Footer with address, contact, quick links and policies	Global footer with address, contacts, quick links, policies, accessibility statement and sitemap	Complied
22	3	Admin login	Login-protected portal with session control, throttling and renamed admin path	Complied
23	3	Dashboard	Overview of new enquiries, pending and expiring items, storage and recent activity	Complied
24	3	Payment gateway	Settings module and integration hook provisioned; live integration on confirmation of purpose and provider (Section 17)	Clarification
25	3	News, notices, tenders, recruitments, events	Full CRUD with language variants, scheduling,	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



#	SOW clause	Requirement	Proposed solution	Status
		management	attachments and archive	
26	3	Downloads and gallery management	Media library with categories, ordering, alt text and bulk upload	Complied
27	3	Slider / banner management	Home slider with ordering, link targets, alt text and active window	Complied
28	3	Important links management	Add, order and group external links	Complied
29	3	Incubation Labs management	All 24 labs with every field in SOW clause 4, including status and brochure	Complied
30	3	Enquiry submissions view	Filterable list by form type, lab and status, with detail view, notes and CSV export	Complied
31	3	PDF / image upload support	Type and size validated uploads, no execute permission, virus-safe handling	Complied
32	3	Basic role-based access	Super Admin, Content Editor, Labs Manager and Enquiry Desk roles	Complied
33	3	Website settings management	Site title, favicon, contacts, address, social handles, footer policies, language toggles	Complied
34	3	Email settings management	Provider, API key, sender identity, admin notification address, enable/disable and test email	Complied
35	4	Lab fields: name, number, category, description, images	All maintained per lab with trilingual text and accessible image alt text	Complied
36	4	Facilities, equipment list, suitable-for tags	Repeatable structured lists, filterable on the listing page	Complied
37	4	Brochure PDF and contact details	Versioned brochure upload plus lab in-charge contact block	Complied
38	4	Lab status: Available / Occupied / Coming Soon	Status field driving badges, sort order and the enquiry call-to-action	Complied
39	4	Enquiry button / link	Enquiry pre-tagged with	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



#	SOW clause	Requirement	Proposed solution	Status
		per lab	lab number and name	
40	5	Four enquiry forms with submissions stored in admin	Contact, incubation, industry collaboration and cohort application — all persisted before notification	Complied
41	5	Email notification via SendGrid or Resend API	Provider selectable in settings; acknowledgement to enquirer and alert to admin, with retry on failure	Complied
42	6	Email configuration in admin, API key not exposed	Key stored server-side in environment configuration, masked in UI, never returned to the frontend	Complied
43	7	Cloudflare Turnstile on contact, incubation and industry forms	Turnstile widget plus mandatory server-side token verification and honeypot fields	Complied
44	8	Cloud server, deployment, database, SSL, DNS, backup, hardening	Full deployment scope with separate public and admin URLs and documented runbooks	Complied
45	9	Cloudflare DNS, SSL/TLS, HTTPS redirect, WAF, bot protection, rate limiting, admin path protection, caching	Configured at the edge as listed, with rules reviewed during maintenance	Complied
46	10	SEO: friendly URLs, titles, meta, sitemap, robots, Open Graph, favicon	Implemented per language, with canonical handling across the three locales	Complied
47	10	Performance: optimised images, responsive, mobile-friendly	Image pipeline, caching, minification and a page-weight budget per template	Complied
48	11	Social media content creation, posting, management, live streaming	Monthly content calendar, scheduled posting and live-stream support across all five platforms	Complied
49	12	Maintenance: uptime, server, SSL, Cloudflare, backup monitoring	Monitored with alerting; monthly backup verification and service report	Complied
50	12	Bug fixing, minor updates, admin	Covered under maintenance, with	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672




#	SOW clause	Requirement	Proposed solution	Status
		assistance, content uploads	content supplied by CICM	
51	12	Basic security review and CMS / email / form support	Periodic review, dependency patching and admin support desk	Complied



05 Information Architecture

The full sitemap, three languages deep, with the lab module at its centre.

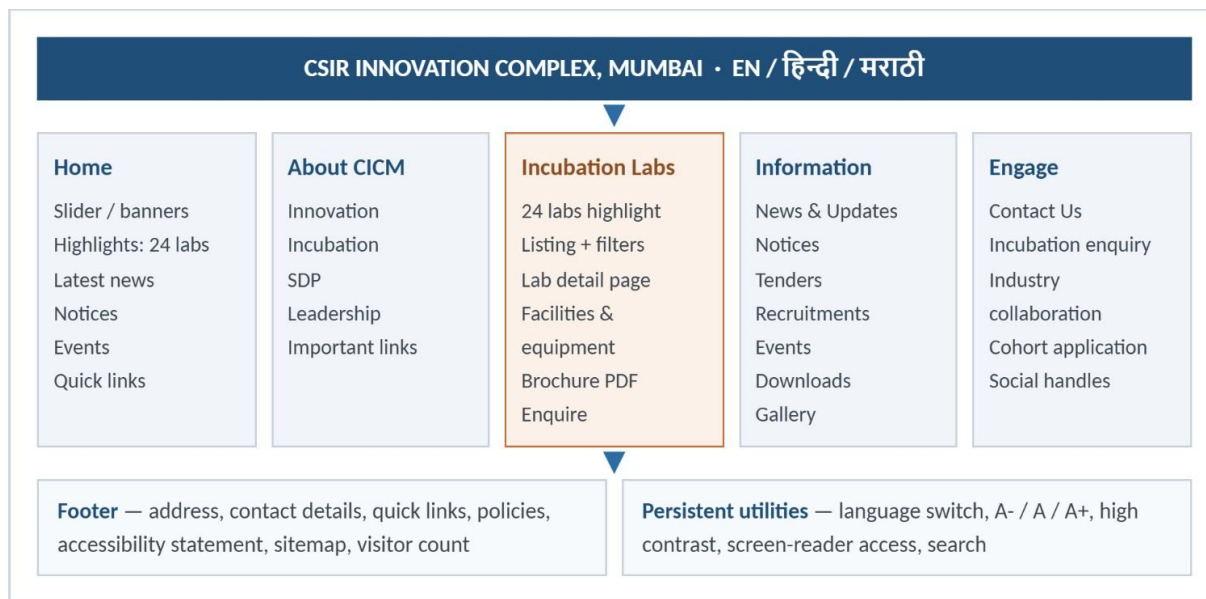


Content types behind the pages

Content type	Fields managed in the CMS
Incubation Lab	Name, lab number, category, description, images, facilities, equipment list, suitable-for tags, brochure PDF, status, contact details, enquiry link
News / Notice / Tender / Recruitment	Title, reference number, summary, body, publish and expiry dates, attachments, language variants, pinned flag
Event	Title, date and time, venue, description, banner, gallery link, registration or enquiry route
Download / Gallery item	Title, category, file or image, alt text, size and format, display order
Enquiry submission	Form type, applicant details, message, related lab, timestamp, status, internal notes, export



06 Solution & Technology Architecture

Cloudflare at the edge, application and CMS in a MeitY-approved cloud in India.

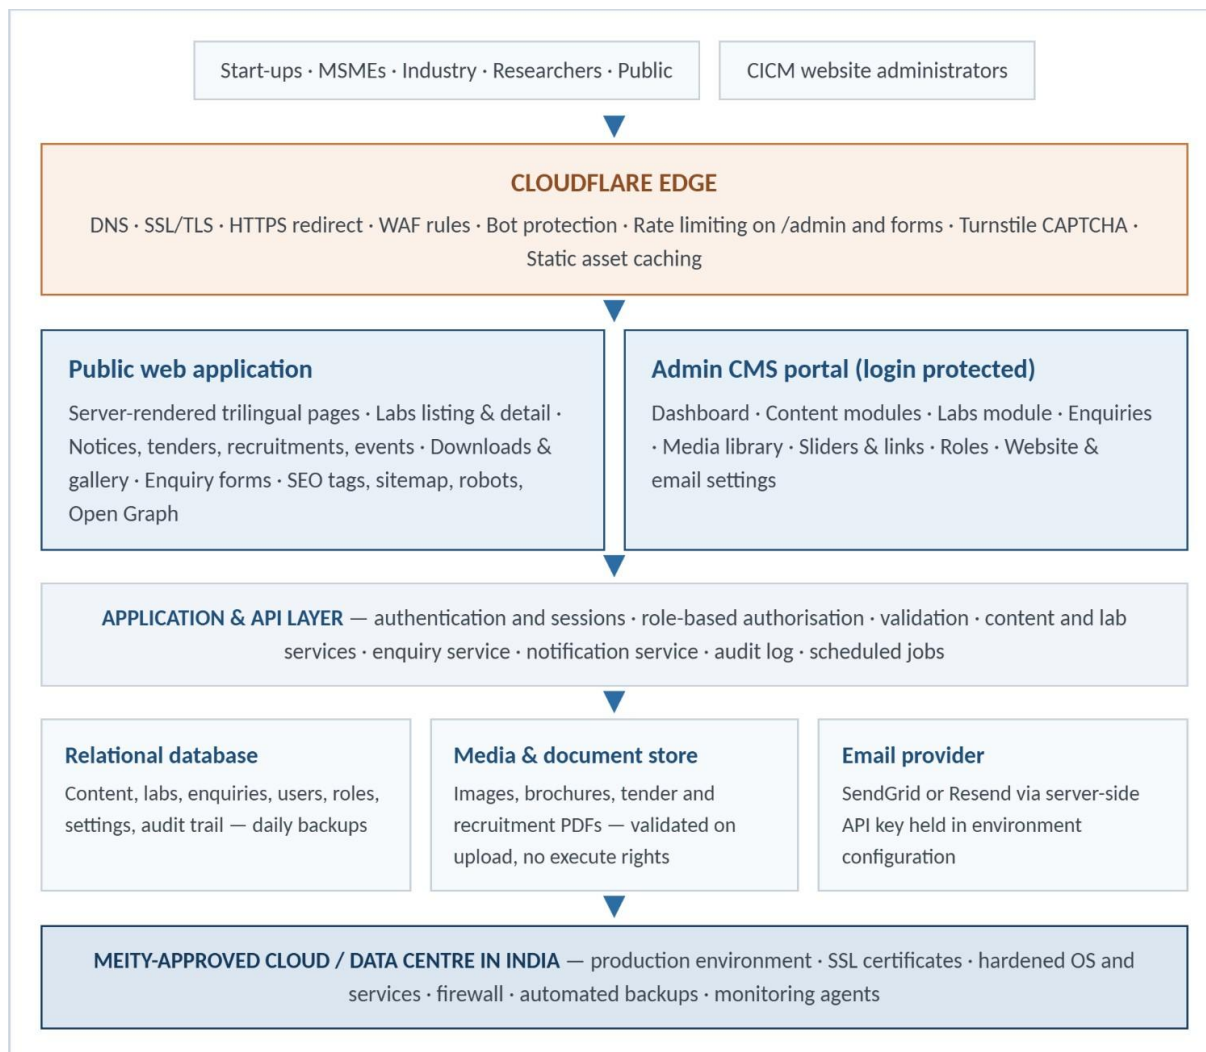

Technology approach

The Scope of Work does not prescribe a technology stack, so we propose an **open-source, licence-free stack** and treat the specific choice as indicative, to be confirmed with CICM during Phase 1 so it fits the approved hosting environment and the institute's own IT preferences.

Layer	Indicative choice (to be finalised in Phase 1)
Frontend	Server-rendered responsive templates, progressive enhancement, no paid UI licences
Application & CMS	Custom-built admin portal on an open-source framework — no third-party CMS licence, no recurring cost to CICM
Database	Open-source relational database with scheduled dumps and point-in-time recovery where supported
Edge & security	Cloudflare DNS, SSL/TLS, WAF, bot management, rate limiting, Turnstile




Layer	Indicative choice (to be finalised in Phase 1)
Notifications	SendGrid or Resend, selectable in the admin email settings with a test-email action




07 Data Flow Diagrams

Context level, then the two flows that carry the project: enquiry handling and content publishing.


DFD Level 0 — context

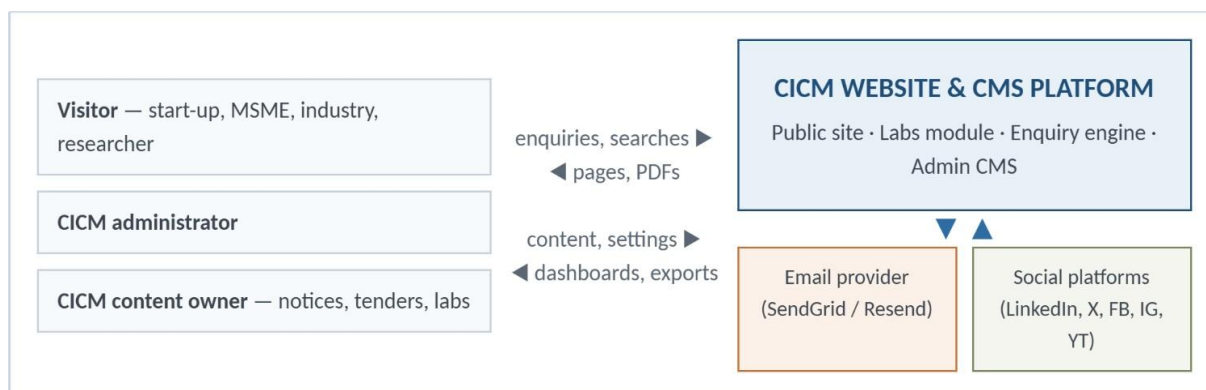

DFD Level 1 — enquiry submission and notification

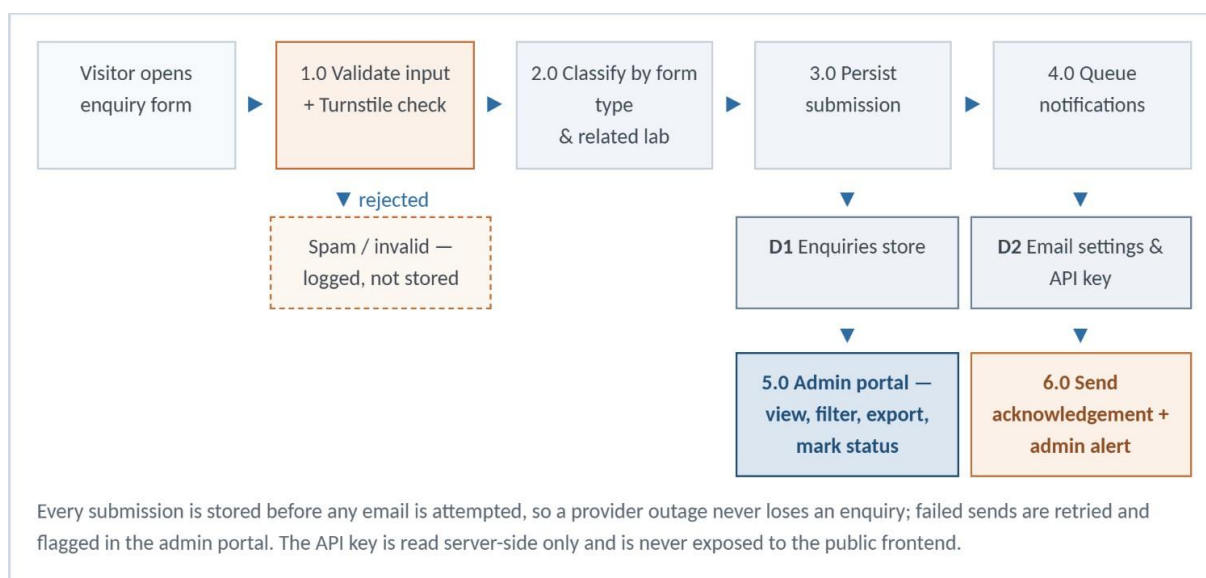

DFD Level 1 — content publishing

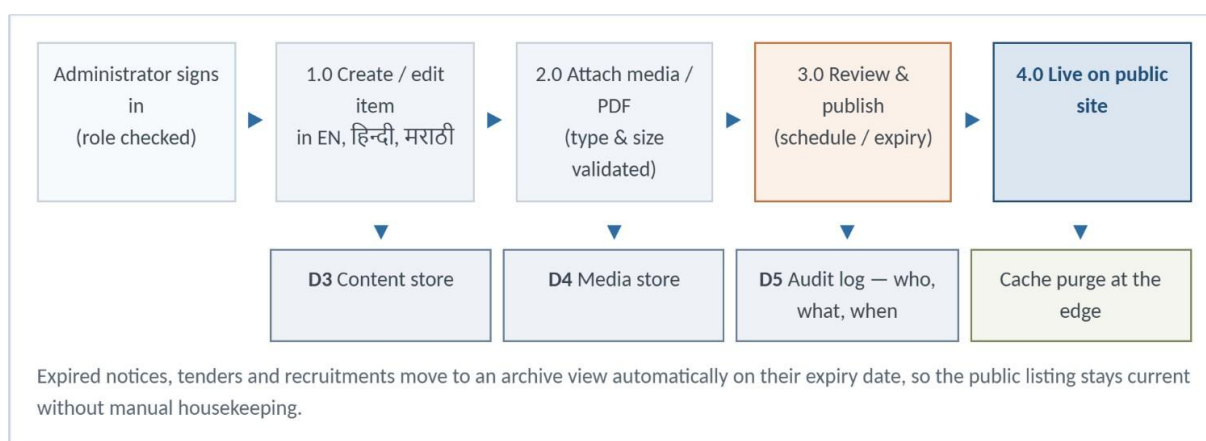



08 Public Website — Modules & Features

Every page named in the Scope of Work, with what it does.

Module	What the visitor gets
Home page	Trilingual landing with slider/banners, a prominent 24-labs highlight, latest news, notices, events, quick links and the three-pillar introduction to Innovation, Incubation and SDP
About CICM	Institutional profile with three dedicated modules — Innovation, Incubation and Skill Development Programme — plus leadership and mandate
Incubation Labs	24-lab highlight, filterable listing page and a detail page per lab with facilities, equipment, images, brochure, status and enquiry route (Section 09)
News & Updates	Dated, paginated listing with detail pages, attachments and social sharing
Notices / Announcements	Reference-numbered listing with publish and expiry dates, PDF attachments and automatic archival
Tenders	Tender listing with reference, dates, corrigenda and downloadable documents
Recruitments / Careers	Advertisement listing with eligibility, last date, application document downloads and archive
Events	Upcoming and past events with date, venue, banner, description and gallery links
Downloads	Categorised document repository with file type, size and download counts
Gallery	Photo and video gallery grouped by event or theme, with accessible alt text
Important Links	Curated external links — CSIR, ministries, Startup India, MSME and partner portals — managed from the CMS
Social media handles	LinkedIn, X, Facebook, Instagram and YouTube presence linked site-wide and surfaced in the footer and contact page
Contact Us	Address, phone, email, map, officer directory and the general contact form
Enquiry forms	Start-up / MSME incubation enquiry, industry collaboration enquiry, general contact and start-up cohort application — all Turnstile protected
Footer	Address, contact details, quick links, policies, accessibility statement, sitemap and visitor count

09 The 24 Incubation Labs Module

The centrepiece of the site: discovery, comparison, and a direct route to enquiry.



Fields the admin controls

Lab name	Trilingual
Lab number	Unique identifier
Lab category	Managed list, filterable
Description	Rich text
Lab images	Gallery with alt text
Available facilities	Repeatable list
Equipment list	Name, make, capability
Suitable for	Start-ups / MSMEs / Industries / Researchers
Brochure PDF	Versioned upload
Lab status	Available / Occupied / Coming Soon
Contact & enquiry	Officer details + enquiry button

Status is a first-class signal

Available — shown with a green marker, listed first, enquiry button prominent

Occupied — visible for reference with expected release note, enquiry routed to waitlist

Coming Soon — announced with a "notify me" enquiry option

Why this matters

A start-up evaluating incubation asks three questions: is there space, does it have the equipment I need, and who do I talk to. The listing answers the first with status filters, the detail page answers the second with a real equipment list and brochure, and the enquiry button — pre-tagged with the lab number — answers the third without the visitor having to explain which lab they mean.



10 Admin CMS Portal

One login, everything the SOW asks an administrator to control.

Access & overview Admin login with session control · Dashboard: enquiries today, pending items, expiring notices, storage · Role-based access	Content management News · Notices · Tenders · Recruitments · Events · Downloads · Gallery · Slider / banners · Important links	Labs & enquiries Incubation labs management (all 24) · Enquiry submissions with filters, status and export · PDF and image upload
Website settings Site title, favicon, contact details, address, social handles, footer policies, quick links, language toggles	Email settings Provider (SendGrid / Resend) · API key (stored server-side) · sender email and name · admin notification address · enable/disable · test email	Payment gateway Provisioned as a settings module and integration hook; the live integration follows CICM's confirmation of purpose and chosen PG — see Section 17

Roles

Role	Can do
Super Admin	Everything, including users, roles, website and email settings
Content Editor	Create and publish news, notices, tenders, recruitments, events, downloads, gallery
Labs Manager	Maintain the 24 lab records, statuses, equipment and brochures
Enquiry Desk	View, filter, update status and export enquiry submissions only



11 Enquiry, Email & Anti-Spam

Four forms, one pipeline, no exposed keys.

Form	Captured	Routed to
General contact enquiry	Name, organisation, email, phone, subject, message	Admin portal + notification inbox
Start-up / MSME incubation enquiry	Entity type, sector, stage, lab of interest, requirement, contact details	Incubation desk
Industry collaboration enquiry	Company, area of collaboration, facility or equipment needed, timeline	Business development desk
Start-up cohort application	Team, idea summary, traction, supporting document upload	Cohort selection committee

Email configuration

Configured entirely from the admin panel: provider choice between SendGrid and Resend, API key, sender email and name, admin notification address, an enable/disable switch and a test-email action that reports the provider's response.

The API key is written to server-side environment configuration, never rendered into a public page, never returned by a public endpoint, and masked in the admin UI after saving.

Spam protection

Cloudflare Turnstile is applied to the contact form, the incubation enquiry form and the industry collaboration form, with keys held in backend or environment configuration. Server-side verification of the Turnstile token is mandatory — a submission without a valid token is refused.

Turnstile is reinforced by Cloudflare rate limiting on form endpoints, honeypot fields and server-side validation of every input.

12 Security, Hosting & Compliance

MeitY-approved hosting, Cloudflare at the edge, and the three certifications the SOW requires.



Area	What we implement
Certifications	IAAP certified accessibility audit as a pre-requisite; GIGW 3.0 conformity established through CQW certification from the STQC Directorate; cybersecurity certification from an auditor empanelled by CERT-In / STQC. We prepare the evidence pack, coordinate the audits and remediate findings at no extra cost within the project.
Hosting & deployment	MeitY-approved data centre or cloud in India: cloud server setup, application deployment, database setup, SSL certificate configuration, domain and DNS support, backup configuration, basic server hardening, production environment setup, separate public and admin URLs.
Cloudflare	DNS setup, SSL/TLS configuration, forced HTTPS redirection, baseline WAF rules, bot protection, rate limiting on sensitive paths, dedicated protection for the admin login path, static asset caching rules and Turnstile integration.
Application security	Server-side validation on every input, parameterised queries, output encoding, CSRF tokens, secure and HttpOnly session cookies, password hashing, login throttling, renamed admin path, upload type and size validation with no execute permission, security headers, and no stack traces or source in error pages.
Backup & recovery	Automated daily database and media backups with retention, off-server copies, documented restore procedure, and monthly restore verification during maintenance.
Accessibility	Semantic markup, keyboard operability, visible focus, contrast validation, alt text discipline, skip links, screen-reader access page, A- / A / A+ text sizing and a high-contrast mode — carried across all three languages.

13 Multilingual, SEO & Performance

Three languages treated equally; discoverability and speed engineered in.

Multilingual architecture

Every content type carries language variants for English, Hindi and Marathi. The language switch preserves the visitor's current page rather than dumping them on the home page, and falls back gracefully with a clear notice when a translation has not yet been supplied.

Unicode fonts throughout, so Devanagari renders on any device with no font download; language-specific metadata, URLs and sitemaps; and CMS fields grouped per language so an editor never has to leave the record to complete a translation.

SEO & performance setup

SEO-friendly URLs	Page titles & meta descriptions
sitemap.xml	robots.txt
Open Graph tags	Optimised images
Responsive design	Mobile-friendly layout
Favicon & site title	Caching & asset minification

Scope note: the Scope of Work asks for basic SEO and performance setup. We implement exactly the listed items — friendly URLs, titles and meta descriptions, sitemap.xml, robots.txt, Open Graph tags, optimised images, responsive and mobile-friendly layout, favicon and site title — plus caching and asset minification as part of basic optimisation.



14 UI Design Concepts & Mock Screens

Three design variants for the public website, each shown as a home page and an inner page, plus the admin CMS. Final selection rests with CICM in Phase 1.

All three variants carry the same information architecture, the mandatory Government of India identity band, the accessibility controls and the trilingual switch. They differ in what the home page leads with — institutional identity, the incubation offer, or search and density — and each carries its own colour treatment.

	Variant 1 — Institutional	Variant 2 — Innovation Forward	Variant 3 — Access & Density First
Home page leads with	CSIR identity, a lab-availability panel and the 24-lab headline	Three action tiles: incubate, collaborate, join a cohort	A full-width search bar and an eight-tile section index
Palette	Deep navy with terracotta accents	Warm terracotta and cream	Dark slate-green with sage accents
Inner page shown	Labs listing — filter chips and lab cards	Lab detail with a pre-tagged enquiry panel	Labs listing with a filter rail, tuned for scanning
Best suited to	A formal CSIR institutional presence	Driving incubation and industry enquiries	Heavy notice, tender and document traffic

Variant 1 — Institutional

CSIR identity first: formal, spacious, hierarchy-led.

HOME PAGE

INNER PAGE — INCUBATION LABS LISTING



Notes: Government identity band, a live lab-availability panel, the three pillars — Innovation, Incubation, SDP — and notice, tender and recruitment boards below. The listing page filters by category, status and suitability.

Variant 2 — Innovation Forward

Action-led: incubation, collaboration and cohort routes above the fold.

HOME PAGE

HOME PAGE

INNER PAGE — LAB DETAIL

INNER PAGE — LAB DETAIL

Notes: A warm identity that opens with what the visitor wants to do. The lab detail page carries facilities, equipment, suitability and a Turnstile-protected enquiry form pre-tagged to that lab number.

Variant 3 — Access & Density First

Search-led, high contrast, built for heavy notice and document traffic.

HOME PAGE

HOME PAGE

INNER PAGE — LABS LISTING (FILTER RAIL)

INNER PAGE — LABS LISTING (FILTER RAIL)

Notes: Search and accessibility controls hold permanent prominence, the section index is one tap from the top, and long notice, tender and document sets stay scannable with date, type and direct PDF download.

New Jersey, USA — Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672




Admin CMS Portal

admin experience.

Common to all three variants — the public theme does not change the

ADMIN CMS — DASHBOARD, ANALYTICS & ENQUIRY DESK

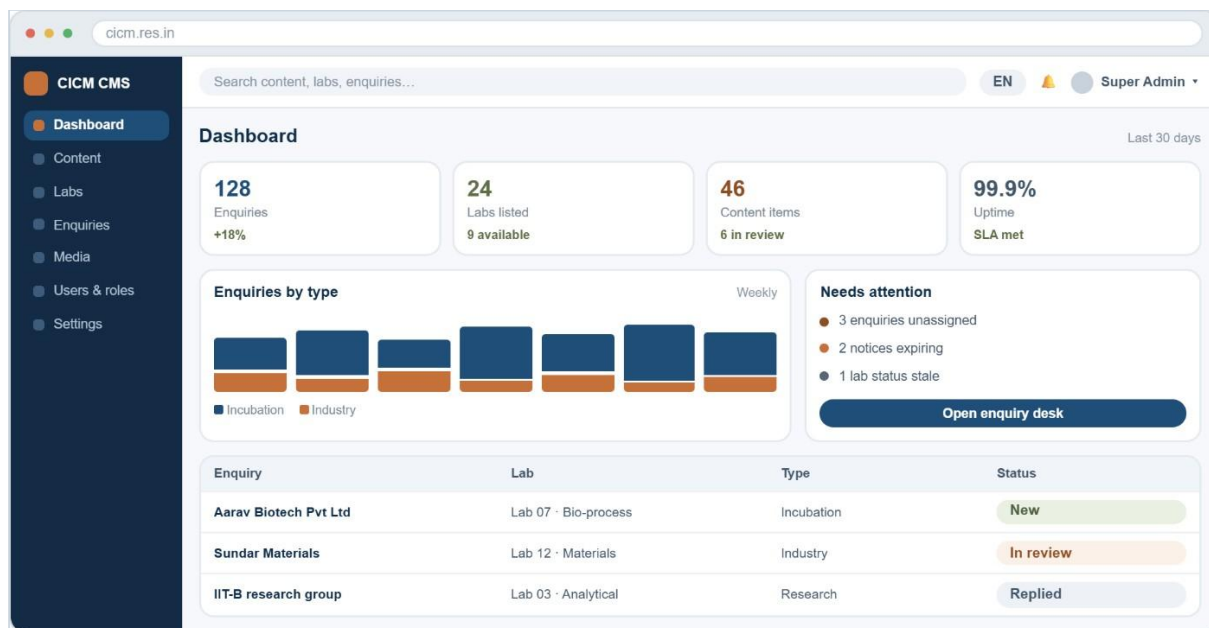

One dashboard for the whole site: enquiry volume by type, items needing attention, and the enquiry desk with status. A responsive mobile view of the home page, labs listing and enquiry form is delivered with whichever variant is approved.

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



15 Implementation Methodology & Timeline

Five phases, gated by design approval and audit clearance.

Phase 1 — Discovery & Design	Weeks 1–3
------------------------------	-----------

Kick-off and governance · content and asset inventory with CICM · information architecture and sitemap · technology confirmation for the approved hosting environment · design options for home page, inner page, labs listing, lab detail and admin dashboard · accessibility-led design review · approval.

Gate: development starts after CICM approves the design.

Phase 2 — Build	Weeks 3–8
-----------------	-----------

Trilingual frontend · admin CMS with all content modules · 24-lab module · four enquiry workflows · email settings and provider integration · Turnstile · media and PDF handling · roles · website settings · SEO and performance setup · content and lab data loading with CICM.

Phase 3 — Deploy & Harden	Weeks 8–10
---------------------------	------------

MeitY-approved cloud provisioning · application and database deployment · SSL and DNS · Cloudflare DNS, WAF, bot protection, rate limiting and caching · server hardening · backup configuration · production and admin URL setup.

Phase 4 — Audit & Certification	Weeks 10–13
---------------------------------	-------------

IAAP accessibility audit · GIGW 3.0 checklist and CQW submission to STQC · cybersecurity audit by a CERT-In / STQC empanelled auditor · remediation and re-test.


Gate: go-live follows audit clearance and CQW certification.

Phase 5 — Go-Live & Maintenance Start	Weeks 13–14
---------------------------------------	-------------

Final content load · production cutover · smoke tests · monitoring switch-on · admin walkthrough of the CMS · start of the annual maintenance term and social-media handling.

16 Annual Maintenance & Support

Monitoring, admin assistance and content support through the maintenance term.



Monitoring & technical support

Website uptime monitoring
Basic server health monitoring
SSL monitoring and renewal alerts
Cloudflare configuration monitoring
Backup monitoring + monthly verification
Bug fixing for developed modules
Basic security review
Basic CMS support and admin assistance
Email configuration support
Form submission monitoring support

Content update support

Content is provided by CICM; we upload and maintain it. Covered items: notices, tenders, recruitment posts, PDF documents, news, events, gallery images, incubation lab content and minor text corrections — plus minor text, image and PDF updates across the site.

Social media handling

LinkedIn, X, Facebook, Instagram and YouTube: content creation, posting and management, and live streaming support for CICM events — coordinated with the website so an announcement, its notice page and its social post carry the same message.

Reporting: a monthly service report covering uptime, incidents and fixes, content updates performed, backup verification, security review notes and social-media activity.

17 Deliverables, Assumptions & Clarifications

What CICM owns at the end, and what we need confirmed.

Deliverables

Approved design set (home, inner, labs, admin)	Trilingual public website, live on approved hosting
Admin CMS portal with role-based access	24 Incubation Labs module, fully populated
Four enquiry workflows with email notification	Cloudflare configuration incl. Turnstile
IAAP accessibility audit report	CQW certificate (GIGW 3.0) from STQC
Cybersecurity audit certificate	Backup and restore configuration + runbook
Admin assistance and content-update support	

Assumptions & dependencies

1	All content — text, images, PDFs, lab data, brochures — and its Hindi and Marathi translations are provided by CICM, as stated in the Scope of Work. We implement, upload, typeset and validate rendering.
2	Cloud subscription on the MeitY-approved provider, domain registration and renewal, Cloudflare plan (if a paid tier is required), email provider plan and certification body fees are borne by CICM; we perform all configuration and coordination.
3	A nominated CICM officer is available for design approval, content sign-off, UAT and audit coordination within the phase windows, so the schedule holds.
4	Audit scheduling by IAAP, STQC and the empanelled cybersecurity auditor is outside our control; we prepare evidence and remediate findings promptly, and report any slippage caused by audit queues.
5	Social-media account ownership, brand approvals and any paid promotion budget remain with CICM; we handle creation, posting, management and live streaming.
6	The solution is delivered on an open-source, licence-free stack, so no recurring licence cost accrues to CICM.

Clarifications sought

Payment gateway. The admin scope lists a payment gateway but the Scope of Work does not state what is being charged for. We have provisioned the settings module and integration hook, and will implement a specific gateway once CICM confirms the purpose (for example event registration, cohort application fee or lab usage charges), the preferred provider and who holds the merchant account. Transaction charges and merchant onboarding are outside this technical scope.

New Jersey, USA – Headquarters
3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE
Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India
B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



Social media scope. We have assumed a monthly content calendar with a posting cadence and live-streaming support for CICM events. Confirming expected volumes — posts per platform per month and number of live streams per year — lets us size the retainer precisely.

Point of contact for this proposal

Source Soft Solutions Private Limited · B-21, CESPL Building, Sector 67, Noida, Gautam Buddha Nagar, Uttar Pradesh – 201301

info@sourcesoftsolutions.com · +91 98999 41672 · www.sourcesoftsolutions.com

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672
