



TECHNICAL PROPOSAL

Website Designing, Development, Deployment and Hosting on Government Web Server as per GIGW 3.0, with Security Certification

Client: ICAR–National Research Centre on Camel (NRCC), Bikaner

Indian Council of Agricultural Research, Ministry of Agriculture & Farmers Welfare, Government of India

Bilingual (English / Hindi) · GIGW 3.0 & STQC certified · CERT-In audited · 1 + 3 years

Submitted By



SOURCE SOFT SOLUTIONS PRIVATE LIMITED

B-21, CESPL Building, Sector 67, Noida, Gautam Buddha Nagar, Uttar Pradesh – 201301

info@sourcesoftsolutions.com · +91 98999 41672 · www.sourcesoftsolutions.com

Submitted in response to the custom bid: Website Designing, Deployment and Hosting (Govt. webserver) as per latest GIGW 3.0 guidelines and all security certification for 1+3 years

Confidential | Technical Bid | No Financial Information Included

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672

Table of Contents

Technical proposal for the design, development, hosting, certification and 1+3 year maintenance of the ICAR–NRCC website.

·	About the Company	Company profile, capabilities and leadership
01	Executive Summary	The proposal in one page, with engagement facts
02	Our Understanding of the Requirement	Audiences, the four dependent phases, scope boundaries
03	Project Objectives	Six outcomes we will be measured against
04	Requirement to Solution Compliance Matrix	Every tender clause mapped to a deliverable
05	Information Architecture	The tender sitemap turned into a navigable structure
06	Solution & Technology Architecture	Presentation, application, CMS, data and hosting layers
07	Data Flow Diagrams	Context level, bilingual publishing and document archival
08	Website Modules & Features	Every module named in the sitemap, with what it does
09	Bilingual Content Model	English and Hindi as equals, published simultaneously
10	Advanced CMS & Role-Based Access	Modules, workflow, roles and audit trail
11	Search, Analytics & e-Portal Integration	Site search, visitor count, Google Analytics, e-portals
12	Security, CERT-In Audit & STQC Certification	Security by design and the certification lifecycle
13	Hosting, Data Centre & Disaster Recovery	Govt/MeitY/NIC hosting, sizing, backup and restore
14	UI Design Concept & Mock Screens	Homepage, inner page, listings, footer and admin CMS
15	Implementation Methodology & Timeline	Four phases inside the 3-month / 6-month limits
16	Testing, Training & Handover	QA, staff training, manuals, source code and NDA
17	Warranty & Three-Year Maintenance	Hypercare, AMC scope, service levels and governance
18	Deliverables, Assumptions & Clarifications	What NRCC owns at the end

How to read this proposal

Section 04 is the compliance record for evaluation — every clause of the tender specification with our response. Sections 06–07 carry the architecture and data-flow diagrams, and Section 14 the mock-up approach with homepage, inner-page and listing screens.



About the Company

Who we are, what we deliver, and the leadership accountable for this engagement.

We at Source Soft Solutions provide AI, cloud, and data solutions to drive innovation and growth across industries. Our services focus on data modernization, analytics, and cloud infrastructure management, helping businesses unlock new possibilities with AI/ML, data insights, and scalable cloud technologies.

Empowering organizations to thrive in the digital landscape.

Headquartered in Edison, New Jersey, with an office in Dubai and our primary engineering centre in Noida, India, we run long-term maintenance and support contracts on the same platforms we engineer — which is exactly the shape of this engagement: build, certify, host and then support for four years.

What we deliver

Transformative Data Solutions	Robust Cloud Services
Advanced AI Capabilities	Insightful Analytics
Seamless Integration	Custom Software Development
Data Security & Compliance	Training & Support

Leadership team



Alok Dharayan · President

25+ years delivering engineering solutions to complex global problems. Masters, New Jersey Institute of Technology. Sets delivery governance and client accountability across Source Soft Solutions' enterprise and government engagements.



Vijay Konar · Chief Technology Officer

Leads all product and platform engineering at Source Soft Solutions. Deep expertise in full-stack development, cloud architecture and data engineering; owns technical standards, release controls and architecture reviews.



Vikram Sharma · Solutions Lead

Architects client engagements end-to-end — from requirement study and solution design to transition-in and steady-state operations. Background in enterprise consulting and large-scale application maintenance programmes.



01 Executive Summary

What we are proposing, in one page.

ICAR–NRC on Camel, Bikaner requires a professional, bilingual, GIGW 3.0-compliant institutional website, deployed and hosted on a Government / MeitY / NIC environment with both Data Centre and Disaster Recovery, audited by a CERT-In empanelled agency, certified by STQC, and then maintained for one year of warranty followed by three years of comprehensive AMC. We propose to deliver exactly that scope as a single accountable engagement — design, build, certify, host, hand over source code, and support.

The website will present the Centre's research, technologies, publications, farmer services and statutory information in English and Hindi simultaneously, on an advanced CMS that NRCC staff operate themselves — with a ten-year archive, role-based access, site-wide search, e-portal redirection, analytics, and an ownership footprint that satisfies GIGW.

01 Bilingual institutional website Home, NRCC Dashboard, Quick Links, Technologies & Services, Units/Sections, Research, Training, Publications, Facilities, For Farmers, Downloads, RTI, About and Contact — every page and document maintained in English and Hindi and published simultaneously.	02 Advanced CMS with role-based access Add, edit, delete and archive any page, notice, tender, circular, publication, gallery item or rate list without a developer; roles for Administrator, Editor, Approver and Unit Contributor; full audit trail.
03 Certified and secure Built to GIGW 3.0 and WCAG from the first wireframe, security-audited by a CERT-In empanelled agency, STQC certified, SSL/TLS secured, with the one-time STQC fee carried in our bid.	04 Hosted with DC and DR Deployment on Govt/MeitY/NIC infrastructure sized at 16 vCPU, 16 GB memory and 500 GB NVMe, with Data Centre and Data Recovery services, scheduled backups and an offline copy on external hard disk supplied by us.

05 1 + 3 years of accountability. One year of warranty and free hypercare from go-live, then three years of comprehensive maintenance covering bug fixing, page addition/deletion/updating, security patching and 24×7 reachability for security incidents — with restoration at our cost in the event of compromise.

Engagement at a glance

Contract shape	4 years 3 months — 3 months design & development, 1 year warranty, 3 years AMC
Hard deadline	Website live within 6 months of award; 3 months from design-template approval
Four delivery phases	Design & development → hosting → CERT-In security audit → STQC certification
Domain	Registration / continuity of www.nrccamel.res.in handled by us
Ownership	Design, technical documents and source code are the property of NRCC; NOC / ownership certificate and NDA signed by us
Eligibility	MeitY empanelment per O.M. 3(26)/2024-EG-II and GIGW-

New Jersey, USA – Headquarters
3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE
Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India
B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



	compliant Govt./ICAR website experience evidenced with the bid
--	--

02 Our Understanding of the Requirement

A certified government platform for a research institute — not a brochure site.

Reading the tender specification, this engagement has four dependent parts, and the risk sits in the joins between them. The website must be **designed and built** to GIGW 3.0 with mock-ups approved before development; it must then be **hosted** on Government/MeitY/NIC infrastructure with Data Centre and Data Recovery; it must clear a **security audit by a CERT-In empanelled agency**; and it must obtain **STQC certification**, with the vendor carrying the certification fee and closing every shortcoming the certifying authority raises. Payment follows the same chain — 70% only after the site is live with initial certifications in hand.

Our governing principle: certification is a design constraint, not a final exam. Accessibility, security and archival behaviour are built into the first wireframe so that STQC and CERT-In findings are confirmations, not rework.

Who the website serves

Farmers & camel rearers	Researchers & students	Industry & entrepreneurs	Staff & public bodies
Advisories, success stories, helpline, product and technology rate lists — mostly on a phone, often on a weak connection	Projects, research achievements, publications, Vision 2050, annual reports, training calendar	ICAR-certified technologies, ITMU, technology rate list, tenders and contracts	Employee Corner e-portals, RTI, vigilance and grievance information, notices, office orders, tourist corner

What is in scope — and what we need confirmed

In our scope	Dependencies & clarifications
Mock-ups and design finalisation · bilingual frontend · advanced CMS with role-based access · content import/creation and migration of existing content · site search · error handling · analytics and visitor counter · social media and e-portal redirection · archival system (10 years) · SSL · security hardening · CERT-In audit coordination and remediation · STQC/GIGW certification including the one-time fee · deployment and hosting on Govt/MeitY/NIC with DC and DR · backups including external hard disk · staff training · user and technical manuals · source-code handover · NDA and ownership certificate · 1-year warranty and 3-year AMC	Content, photographs and Hindi translations are supplied by NRCC (we implement, structure and upload them, and can supply translation as a priced option). Government hosting allocation, NIC/MeitY account provisioning and any data-centre charges levied directly on the Institute sit with NRCC. Credentials for e-Office, e-HRMS, SPARROW, PFMS, CPP, ARMS and Samarth are linked, not integrated, unless a specific integration is defined. The page count may increase or decrease; we have priced a flexible page model rather than a fixed count.



03 Project Objectives

Six outcomes we will be measured against.

Objective 01 — A professional institutional presence A clean, uncluttered, DBT/DST-class layout that presents a large volume of content without crowding, and that works on every major browser, operating system and screen size.	Objective 02 — True bilingual parity English and Hindi treated as equals in the CMS and on the frontend, with Unicode rendering, language-aware navigation and simultaneous publication of pages and documents.
Objective 03 — Independent content control NRCC staff add, edit, delete, archive and re-order content themselves through an advanced CMS, with the architecture explained to NRCC technical personnel so they can customise it day to day.	Objective 04 — Certifiable compliance GIGW 3.0, WCAG as applicable under GIGW, STQC certification and CERT-In security clearance obtained before go-live and maintained through the contract.
Objective 05 — Resilient hosting Government hosting with Data Centre and Data Recovery, tested restores, scheduled backups and 24×7 reachability for any security loophole or compromise.	Objective 06 — Institutional ownership Source code, design files, technical documentation, credentials and a full backup handed to NRCC, with NDA and ownership certificate, so the Institute is never locked to a vendor.



04 Requirement to Solution Compliance Matrix

Every clause of the tender specification, mapped to what we will build.

#	Clause	Tender requirement	Our solution	Status
1	Eligibility	Only MeitY-empanelled firms per O.M. 3(26)/2024-EG-II dated 27.11.2024, endorsed by ICAR, are technically qualified	Bid submitted as a MeitY-empanelled entity; empanelment evidence and ICAR/Govt. GIGW website experience of the last three financial years enclosed with supporting documents	Complied
2	Design	Professional layout comparable to DBT/DST websites	Three mock-up variants for homepage and inner pages, built on a government-grade design system: identity band, clear hierarchy, generous whitespace, no clutter	Complied
3	Design	Cross-platform and cross-browser compatibility	Tested on Chrome, Edge, Firefox and Safari across Windows, macOS, Android and iOS; no browser-specific dependencies	Complied
4	Design	Mobile device compatibility; responsive and fluid design; desktop, notebook, tablet, smartphone	Fluid responsive layout with breakpoint testing on real devices; touch targets, readable type and low-bandwidth image delivery	Complied
5	Design	Bilingual interface (English & Hindi)	Language-aware routing, Unicode Devanagari throughout, per-language metadata and a CMS that holds both language fields on one record	Complied
6	Design	Large volume of pages accommodated; pages may increase or decrease	Template-driven page model with unlimited pages, sections and menu depth; no per-page development effort	Complied
7	Design	Website should accommodate different themes (colours, fonts) for different occasions	Theme switcher in the CMS: seasonal/occasion palettes and a national-mourning greyscale mode applied site-wide from a single setting	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



#	Clause	Tender requirement	Our solution	Status
8	Design	Ownership information displayed in header/footer	Ownership, copyright © NRCC, last-updated stamp and CMS-controlled footer identity on every page	Complied
9	Function	Search feature; site search optimised	Site-wide indexed search across pages, notices, tenders, publications and documents, with filters by section, date and language	Complied
10	Function	Error handling	Friendly bilingual 404/500 pages with search and navigation, plus server-side logging of every error for the support desk	Complied
11	Function	Import / creation of content	Content audit of the existing site, cleaning, optimisation and structured migration; new content created in the CMS templates	Complied
12	Function	Advanced CMS portal to manage content — delete/edit/update	Role-based CMS with create, edit, delete, restore, schedule and archive on every content type, with preview before publish	Complied
13	Function	Role-based management module	Administrator, Editor, Approver, Unit Contributor and Read-only roles; per-module permissions and full audit trail	Complied
14	Function	Redirection to NRCC social media (Facebook, Instagram, YouTube, X, LinkedIn)	CMS-managed social handles, follow buttons in header/footer and share buttons on every content page	Complied
15	Function	Redirection to e-portals: e-Office, e-Sparrow, e-HRMS, NIC email, PFMS, CPP Portal, ARMS, Samarth	Employee Corner with a CMS-managed link registry, opening each portal in a new secure context; link health monitored monthly	Complied
16	Function	Capable of redirecting to / hosting other project websites and mobile apps	Sub-site and micro-site support under the same domain, plus an app-links section for	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



#	Clause	Tender requirement	Our solution	Status
			Android/iOS applications	
17	Function	Archival system with access to at least the last 10 years	Automatic archival by publication date with a public archive browser filtered by year, section and language; archived items stay searchable	Complied
18	Function	Flexible addition/deletion of pages and content	Menu builder and page composer in the CMS; adding a section is a content task, not a development task	Complied
19	Function	Static and dynamic pages both considered	Static institutional pages and dynamic listings (news, tenders, projects, publications, gallery) driven from structured records	Complied
20	Function	Visitor count and Google Analytics	Public visitor counter plus Google Analytics 4 with section-wise dashboards for the administrator	Complied
21	Function	Social media enabled web content	Open Graph metadata, share actions and embeddable media on every page	Complied
22	Accessibility	Web content accessibility; specially-abled friendly as per GoI norms; WCAG per GIGW 3.0	Screen-reader access page, skip-to-content, keyboard operability, text resize (A- A A+), high-contrast mode, alt text discipline and accessibility audit before go-live	Complied
23	Performance	Minimal loading time (click to response)	Optimised images, caching, compression, minified assets and query tuning; performance budget validated on 3G-class connections	Complied
24	Security	Security, data protection, privacy and data backup integrated	Input validation, secure sessions, HTTP-only cookies, security headers, encrypted transport, least-privilege database access and scheduled backups	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



#	Clause	Tender requirement	Our solution	Status
25	Security	SSL certification for enhanced security	Site-wide SSL with HTTPS redirection and TLS 1.2+ ciphers; certificate renewal tracked through the AMC	Complied
26	Security	Security audit by a CERT-In empanelled agency	Audit coordinated and paid for by us, findings remediated and re-tested until a clean clearance certificate is issued	Complied
27	Security	Developer reachable 24x7 for security loopholes; restoration at vendor cost after compromise	24x7 security contact, monitored alerts, and restoration from verified backups at our cost in the event of hacking, compromise or crash	Complied
28	Certification	GIGW 3.0 compliance and STQC certification mandatory; vendor undertakes all STQC tasks and fee	GIGW checklist governed from wireframe stage; STQC application, forms, shortcoming closure and the one-time STQC fee carried in our bid	Complied
29	Hosting	Deployment and hosting on Govt/MeitY/NIC servers with Data Centre and Data Recovery	Deployment on the Government environment with DC and DR, documented cutover, and DR drill before go-live	Complied
30	Hosting	Hosting infrastructure — 16 vCPU, 16 GB memory, 500 GB NVMe	Provisioned to the stated sizing with headroom monitoring; scaling recommendations reported to NRCC each half-year	Complied
31	Hosting	Domain name registration / continuity of www.nrccamel.res.in	Domain registration and DNS configuration handled by us, with records handed to NRCC	Complied
32	Hosting	Complete backup provided on external hard disk, cost borne by the vendor	Full site, database and media backup delivered on an external hard disk supplied by us, refreshed at handover and at contract close	Complied
33	Delivery	Four phases: design and	Delivery plan structured	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



#	Clause	Tender requirement	Our solution	Status
		development, hosting, CERT-In audit, STQC certification	as those four phases with an approval gate between each — see Section 15	
34	Delivery	Mock-ups created first for finalisation of homepage and inner pages	Three homepage and inner-page variants presented in the technical bid (Section 14); the approved variant is then developed	Complied
35	Delivery	Design finalised as and when required by NRCC; development within 3 months of template approval; live within 6 months of award	Committed schedule with design iterations, development inside 3 months of approval and go-live well inside the 6-month cap	Complied
36	Delivery	Open-source development platform; platform named in the bid	Open-source stack — PHP/Laravel or Python/Django application with MySQL/PostgreSQL and an open-source CMS layer; the exact platform is declared in the bid and agreed at kick-off	Complied
37	Delivery	Architecture, design and coding algorithm explained to NRCC technical personnel	Architecture walkthrough sessions plus a technical manual covering code structure, deployment and customisation	Complied
38	Delivery	Comprehensive testing	Functional, responsive, cross-browser, bilingual, accessibility, performance, security and UAT cycles with signed test reports	Complied
39	Delivery	Training of NRCC staff	Role-wise training for administrators, editors and unit contributors, with recorded sessions and a quick-reference guide	Complied
40	Ownership	Design, technical documents and source code are NRCC property; NOC / ownership certificate signed; copyright ©	Full source code, design assets and documentation handed over; ownership certificate and NOC executed; copyright	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



#	Clause	Tender requirement	Our solution	Status
		NRCC	notice on every page	
41	Ownership	Non-Disclosure Agreement	NDA signed before content or credentials are shared	Complied
42	Ownership	Non-blacklisting undertaking on ₹100 notarised stamp paper	Undertaking submitted with the bid, notarised and not older than six months	Complied
43	Support	One-year warranty / free hypercare after go-live	Named hypercare team, defect fixes, content assistance and monitoring at no charge for twelve months	Complied
44	Support	Three-year comprehensive maintenance: bug fixing, addition/deletion/update of pages	AMC covering corrective, adaptive and preventive maintenance, content updates, security patching and certificate renewals	Complied
45	Support	Subsequent certifications required for continuous running arranged by the vendor	Renewal of SSL, security re-audit and STQC re-validation arranged by us and reimbursed at actuals per the tender terms	Complied
46	Support	Pre-bid meeting and updating to discuss web content	We will attend the pre-bid meeting and maintain a content register agreed with NRCC through delivery	Complied

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



05 Information Architecture

The tender sitemap, organised so a farmer, a researcher and a staff member each reach their page in two clicks.


nrccamel.res.in — Home (EN / हिन्दी)				
NRCC Dashboard Announcements Tourist Corner Tender / Purchase / Work Contract Media Coverage NRCC in News Directory · Phone / Email Social links · Visitor count	Quick Links Calendar of Events Citizen's Charter Vacancies Holiday Calendar Mobile Apps Photo & Video Gallery Products Rate List	Technologies & Services Technologies Developed ICAR Certified Technologies Technologies Rate List ITMU Success Stories Training Modules	Units & Research Extension · AKMU · Library PME · ITMU · DTPU · CIF Research Units — AGB, CHR Projects (institute, external, contract, international) Research Achievements	For Farmers Successful Entrepreneurs Success Stories Advisories Help Line Products & rate lists
Training / Capacity Training calendar Training modules application Awards & Honors	Publications NRCC Vision 2050 Annual Reports Newsletters Research Papers	Facilities & Cadre Laboratories · Guest House Seminar Hall Cadre strength — sanctioned / in- position / vacant Former Directors	Employee Corner PFMS · e-HRMS 2.0 · SPARROW Notice Board · Office Orders Standing Committees Performa	RTI · About · Contact RTI section 4 information CPIO · Transparency · Vigilance Public Grievance · HRD Nodal About us · Contact us
Footer (GIGW mandatory): Director's Desk · Privacy Policy · Disclaimer · Copyright · FAQs · Site Map · Feedback · Contact Us · Terms of use · Help · Ownership and last-updated stamp · External links: ICAR, ICAR Institutes, NRCC on ICAR · Downloads: Publications, Tenders, Performa				

Navigation principle	How it is applied
Two-click depth	A mega-menu exposes second-level pages directly, so no visitor has to hunt through intermediate landing pages.
Audience shortcuts	Home carries direct entries for Farmers, Researchers, Industry and Employees alongside the institutional narrative.
Breadcrumbs everywhere	Every inner page shows its position and its language twin, so switching language never loses the page.
Growth without restructuring	New units, projects or schemes are added as records inside existing templates; the menu builder places them without code.



06 Solution & Technology Architecture

An open-source stack, deployed on Government infrastructure with Data Centre and Disaster Recovery.

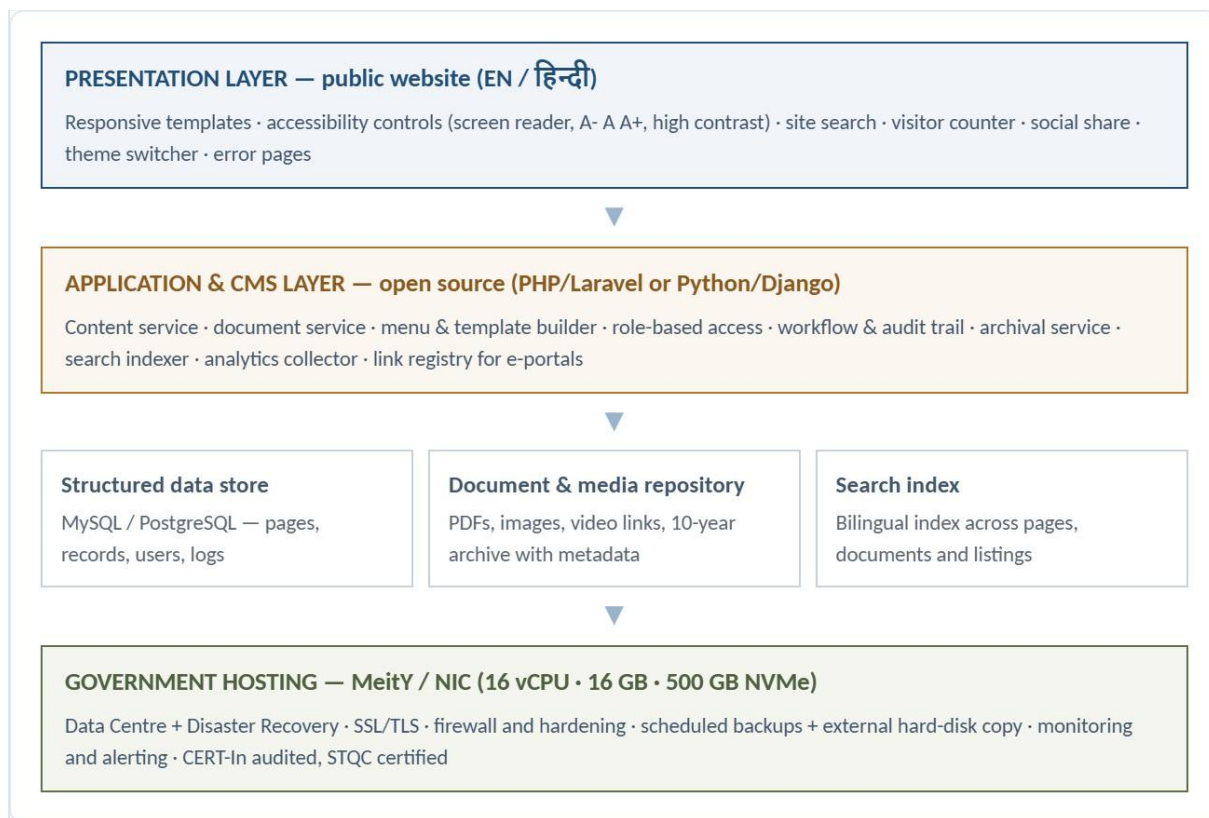

Decision	Why we propose it
Open-source stack	Required by the tender, keeps NRCC free of licence cost, and matches the skills available at ICAR institutes for day-to-day customisation.
Server-rendered pages	Fast first paint on weak rural connections, better accessibility and clean indexing — all of which the GIGW and STQC checks reward.
Template-driven content model	The page count can rise or fall without development, exactly as the tender anticipates.
Sub-site capability	Project websites and mobile-app landing pages can be hosted or redirected under the same domain and the same certification envelope.




07 Data Flow Diagrams

Context level, then the two flows that carry this project: bilingual publishing and document archival.


DFD Level 0 — context



DFD Level 1 — bilingual content publishing

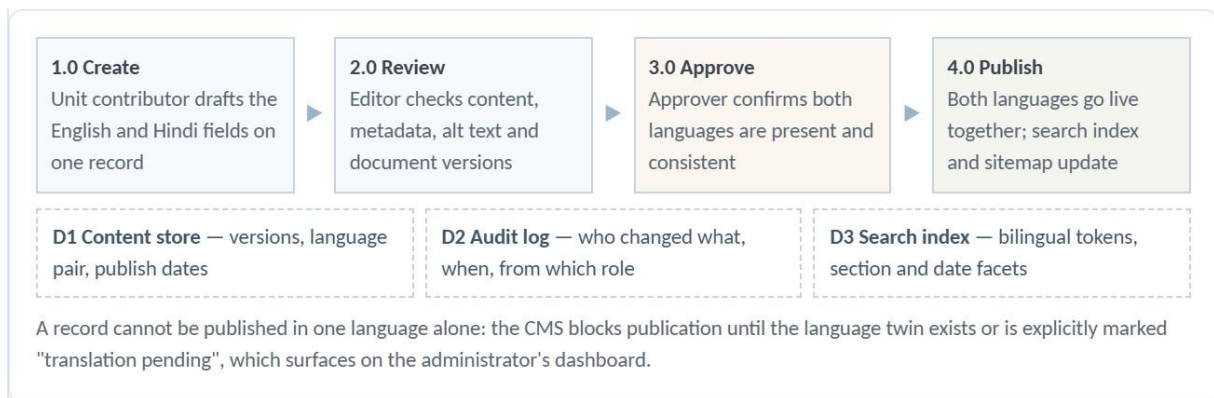

DFD Level 1 — document lifecycle and 10-year archive

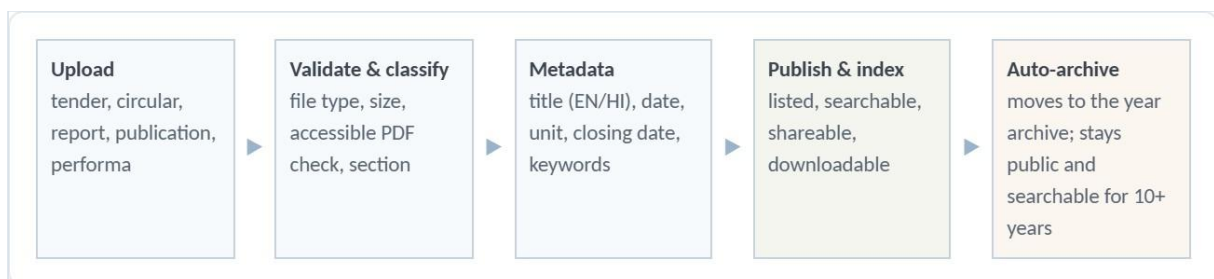

08 Website Modules & Features

Every module named in the tender sitemap, with what the visitor gets and what the administrator controls.

Module	What the visitor gets	What the administrator controls
Home & NRCC Dashboard	Announcements, tourist corner, tenders, media coverage, NRCC in news, directory, social links, visitor count and search	Slider, highlights, order of blocks, expiry dates
Quick Links	Calendar of events, citizen's charter, vacancies, holiday calendar, mobile apps, photo and video gallery, products rate list	Link registry, gallery albums, rate list versions
Technologies & Services	Technologies developed, ICAR-certified technologies, technology rate list, ITMU, training modules, success stories	Technology records with images, rates and status
Units / Sections	Extension, AKMU, Library, PME, ITMU, DTPU, CIF and others, each with its own page and staff	Unit template, contributor assignment
Research	Research units (AGB, CHR), ongoing institute, externally funded, contract and international projects, research achievements	Project records with PI, duration, funding, status
Training & Capacity Building	Training calendar and an online training-module application form	Calendar entries, application inbox and export
Publications	Vision 2050, annual reports, newsletters, research papers, other publications — all downloadable and searchable	Versioned uploads with year and category
Facilities & Cadre	Laboratories, guest house, seminar hall; cadre strength sanctioned / in-position / vacant; former directors	Cadre table maintained as data, not as an image
For Farmers	Successful entrepreneurs, success stories, advisories, help line and product information — mobile-first	Advisory publishing with season tags
Employee Corner	PFMS, e-HRMS 2.0, SPARROW, notice board, office orders, standing committees, performa	Portal link registry with health monitoring
RTI & Transparency	Section 4 information, CPIO, transparency, vigilance, public grievance and HRD nodal officers	Officer records with tenure history
Downloads & Archive	Publications, tenders, performa and other documents, with a ten-year archive browser	Bulk upload, metadata, archive rules



09 Bilingual Content Model

Hindi is not a translation layer bolted on later — it is a first-class field on every record.

How it works

Every page, notice, project, publication and document carries an English field and a Hindi field on the same record. The language switch keeps the visitor on the same page rather than dropping them on the home page, URLs and metadata are language-aware, and Devanagari renders through Unicode with no font download.

Why it matters for this tender

The specification requires documents and pages in bilingual mode to be updated **simultaneously**. A single-record model makes that structurally true instead of dependent on discipline — and the administrator's dashboard lists anything still missing its Hindi twin.

Element	Detail
Navigation & labels	Maintained in the CMS, not hard-coded, so menu names can be corrected in either language without a release.
Documents	Both language versions attach to one record; if only one exists, the listing states which language is available.
Search	Indexed separately per language with a shared record identity, so results never mix scripts confusingly.
Terminology	A shared Hindi glossary for institutional terms keeps translations consistent across units and years.
Accessibility	Language attributes set correctly per block so screen readers switch voice — a GIGW checkpoint that is commonly failed.

10 Advanced CMS & Role-Based Access

One login, everything the tender asks an administrator to control — without a developer.

Content Pages · announcements · notices · office orders · tenders · circulars · media coverage · events · advisories · success stories	Records Projects · technologies · publications · units · staff directory · cadre strength · rate lists · training calendar	Documents & media Upload · metadata · versions · accessible-PDF check · photo and video galleries · 10-year archive
Structure Menu builder · templates · home-page blocks · sliders · footer identity · theme and occasion palettes	Users & roles Administrator · Editor · Approver · Unit Contributor · Read-only; per-module permissions; password policy	Operations Audit trail · analytics dashboard · broken-link report · missing-Hindi report · backup status · link registry

Roles

Role	Can do
Administrator	Everything, including users, roles, menus, templates, themes, settings and archive rules
Editor	Create, edit and publish content across all sections; manage documents and galleries
Approver	Approve or return submissions; confirm bilingual completeness before publication
Unit Contributor	Draft and submit content for their own unit or section only
Read-only / Auditor	View content, audit trail and reports without any change rights

Knowledge transfer clause: the tender requires the software architecture, design and coding algorithm to be explained to NRCC technical personnel. We deliver that as two structured walkthrough sessions plus a technical manual — code structure, database schema, deployment steps, and how to customise templates and content types day to day.

11 Search, Analytics & e-Portal Integration

Discoverability inside the site, measurement of it, and clean routes out to Government systems.

Site search A single indexed search across pages, announcements, tenders, projects, technologies, publications, galleries and archived documents. Filters by section, year and language · document type facets · highlighted matches · a zero-result page that suggests sections rather than dead-ending.	Analytics & visitor count Public visitor counter in the footer, and Google Analytics 4 behind it for the administrator. Section-wise dashboards, most-downloaded documents, search-term report, device and language split, and a monthly summary shared during the AMC.
--	--


Redirection and integration points

Target	Treatment
e-Office, e-Samarth, e-HRMS 2.0, SPARROW, NIC email, PFMS, CPP Portal, ARMS, Samarth	CMS-managed link registry in the Employee Corner; each opens in a new secure context with a clear external-link notice, and link health is checked monthly with a report to the administrator.
ICAR, ICAR institutes, NRCC on ICAR	Standing external links in the footer and Important Links block, maintained from the CMS.
Social media — Facebook, Instagram, YouTube, X, LinkedIn	Follow buttons in header and footer, share actions on every content page, Open Graph metadata for correct previews.
Project websites and mobile applications	Hosted as sub-sites under the same domain, or redirected, with a Mobile Apps page listing Android/iOS links.
Feedback, grievance and helpline forms	Server-side validated forms with spam protection, routed to the configured NRCC mailbox and visible in the CMS inbox with export.



12 Security, CERT-In Audit & STQC Certification

Two certificates stand between development and payment. We plan backwards from them.

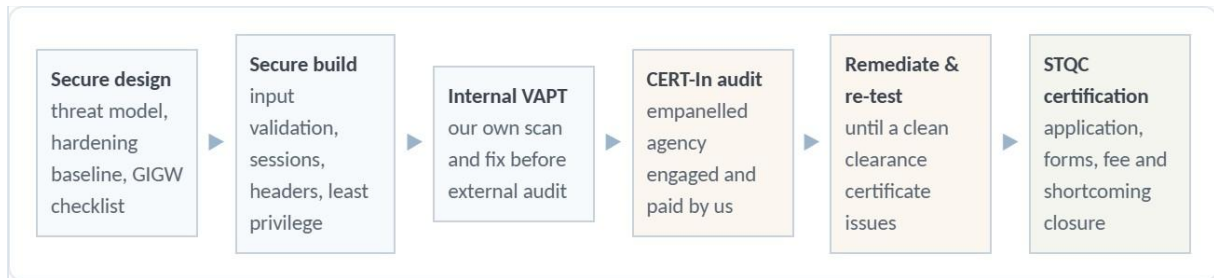

Security controls we implement

Site-wide SSL with HTTPS redirection and TLS 1.2+ ciphers · secure session and HTTP-only cookie handling · server-side input validation and SQL-injection protection · file-upload type and size restrictions with malware scanning · security headers (HSTS, CSP, X-Frame-Options, X-Content-Type-Options) · directory listing disabled · admin panel rate limiting and lockout · secrets kept out of source control · least-privilege database accounts · patched OS and dependencies · centralised error and access logging.

Certification commitments

The security audit is performed by a CERT-In empanelled agency engaged by us. The STQC application, forms, coordination and the **one-time STQC fee are carried in our bid**, and every shortcoming raised by the issuing authority is closed by us at no additional cost. Re-audit after any source-code change, and renewal of SSL and certifications required for continuous running, are arranged by us during the AMC.

Incident commitment: a named engineer is reachable 24×7 for reported security loopholes. In the event of hacking, compromise or crash of the NRCC website, we restore the site from verified backups **at our own cost**, and submit a root-cause note with the corrective action taken.

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



13 Hosting, Data Centre & Disaster Recovery

Government infrastructure, sized as specified, with a recovery path that is tested rather than assumed.

Item	Our provision
Environment	Deployment on Govt / MeitY / NIC infrastructure, with both Data Centre and Data Recovery services obtained as required by the tender
Sizing	16 vCPU · 16 GB memory · 500 GB NVMe storage, monitored for headroom with a capacity note each half-year
Domain & certificates	Registration / continuity of www.nrccamel.res.in, DNS configuration, SSL issuance and renewal tracking
Environments	Staging environment for approval and testing, kept separate from production; nothing reaches production without sign-off
Backup	Scheduled database and media backups with retention, plus a complete offline copy delivered on an external hard disk supplied at our cost at handover and at contract close
Disaster recovery	Documented failover procedure with a DR drill before go-live and one drill each year of the AMC, each with a written result
Monitoring	Uptime, certificate expiry, disk, error-rate and defacement monitoring with alerting to our support desk

Review note: hosting allocation on NIC/MeitY is granted to the Institute, not to a vendor. We therefore treat account provisioning as a joint task with a named NRCC coordinator, and we begin that request in week one so that the audit and certification phases are never waiting on infrastructure.




14 UI Design Concept & Mock Screens

Clean, accessible, responsive and GIGW 3.0-compliant design — homepage, inner page and listing patterns, plus the admin CMS.


The tender requires mock-ups before development begins. The screens below establish the design language: the mandatory Government of India identity band with accessibility and language controls, the ICAR–NRCC masthead with emblem and search, a nine-item mega navigation, and a consistent inner-page pattern of breadcrumb, left section menu and content area. Layout, colour and typography are finalised with ICAR–NRCC in Phase 1 before development starts.

1. Homepage (Desktop)

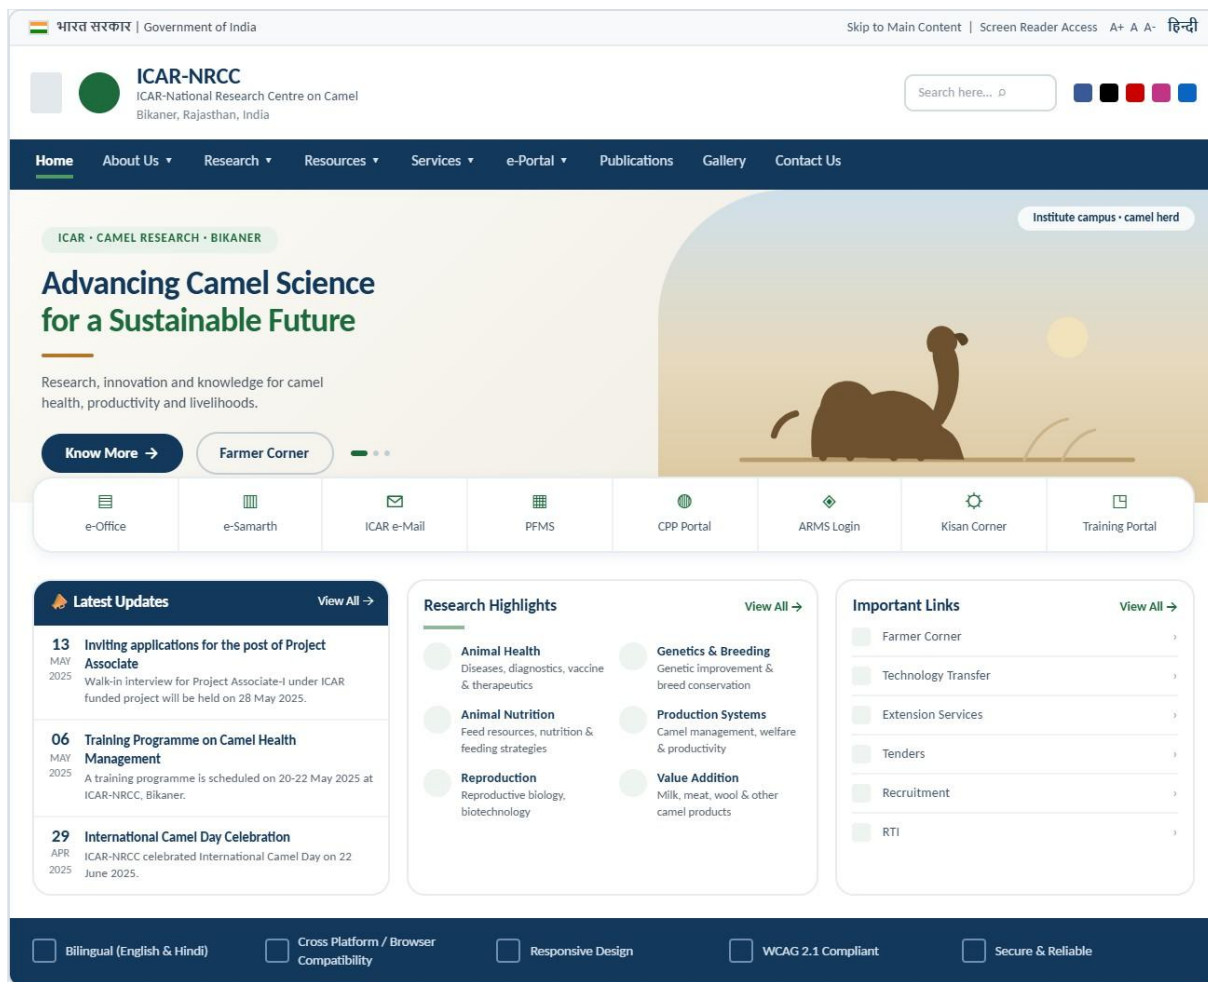


2. About NRCC (Inner Page)


3. Research & Resources (Listing Page)

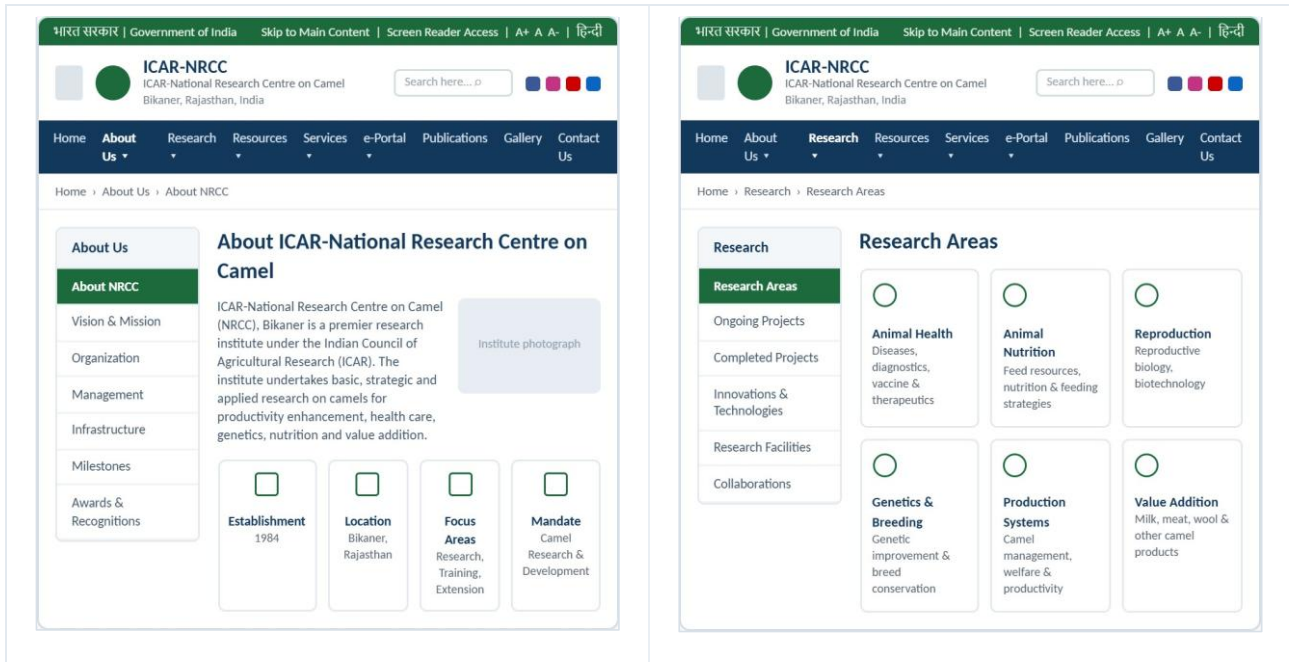

4. News & Updates (Listing Page)

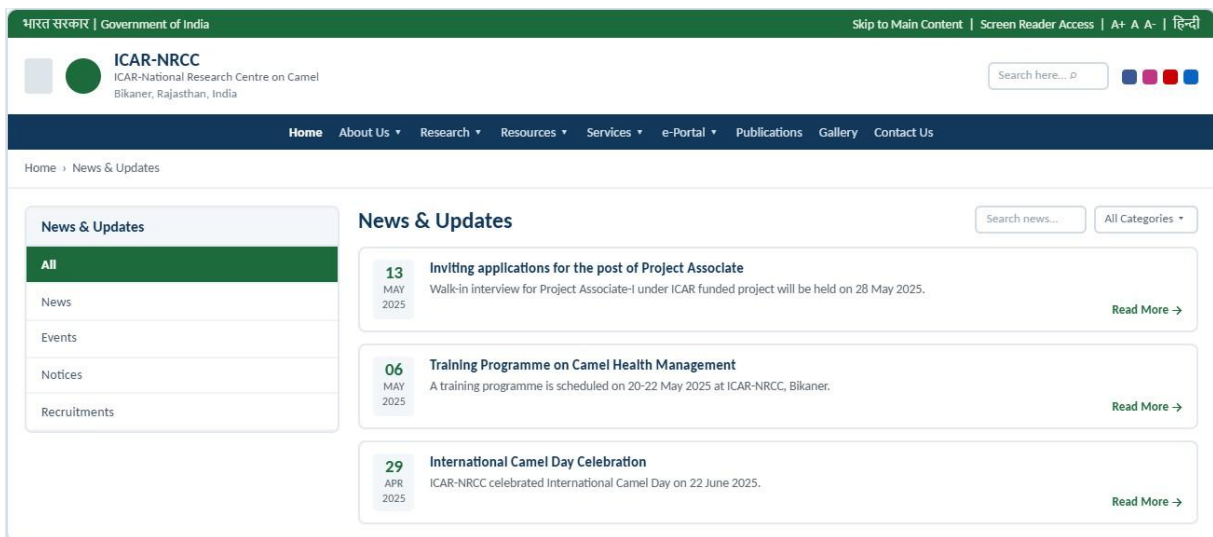

5. Global Footer — ownership, quick links, contact and social



Design element	Why it is there
Gol identity band	Mandatory Government of India strip with Skip to Main Content, Screen Reader Access, text resize (A+ A A-) and the □□□□□ switch — GIGW 3.0 checkpoints that must appear on every page.
Masthead	National emblem, ICAR mark, institute name in both languages, site search and official social handles in one row.

New Jersey, USA – Headquarters
3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE
Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India
B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672




Design element	Why it is there
Mega navigation	Nine top-level groups covering the full tender sitemap, each exposing its second level directly so no page is more than two clicks away.
e-Portal strip	e-Office, e-Samarth, ICAR e-Mail, PFMS, CPP Portal and ARMS reachable from the homepage, maintained as a CMS link registry.
Latest Updates bar	Dated announcement ticker with a View All route into the ten-year archive.
Inner-page pattern	Breadcrumb, left section menu and content area — one pattern reused across About, Research, Publications, Services and RTI, which is what keeps a large site consistent and cheap to extend.
Footer	Ownership and copyright © NRCC, last-updated stamp, Web Information Manager, RTI, tenders, FAQs, sitemap, help, feedback and contact — the GIGW-mandated footer set.

Admin CMS Portal

The same content model, from the administrator's side.

ADMIN CMS — DASHBOARD, BILINGUAL STATUS & CONTENT DESK

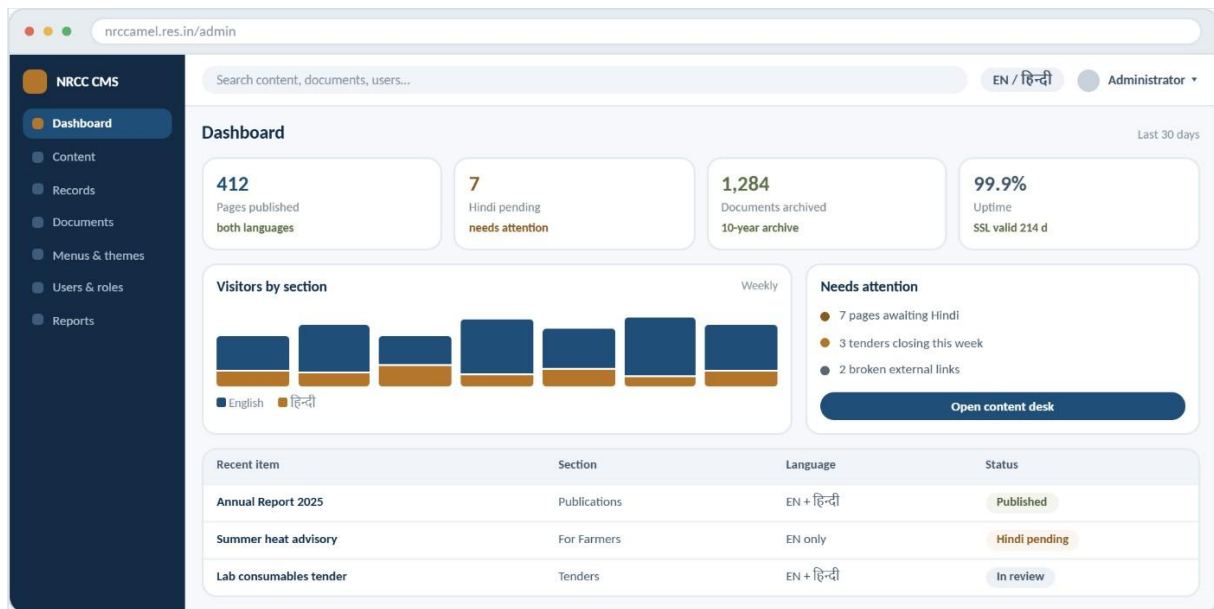

The dashboard is built around the two things that go wrong on bilingual government sites: content published in one language only, and documents that quietly expire. Both are surfaced as work items, not buried in reports.

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672



15 Implementation Methodology & Timeline

The tender's four phases, sequenced so that go-live sits well inside the six-month cap.

Phase 1 — Requirement study, mock-ups and design approval · Weeks 1–4

Kick-off and NDA · pre-bid points closed · audit of the existing site and content inventory · sitemap confirmation against the tender · three homepage and inner-page mock-ups · accessibility and GIGW checklist agreed · **design template approval by NRCC** · hosting and domain request raised with NIC/MeitY in week one.

Phase 2 — Development and content migration · Weeks 4–13 (within 3 months of template approval)

Bilingual frontend build · advanced CMS with role-based access · menu, template and theme builders · search index · archival service · analytics and visitor counter · e-portal link registry · forms · content cleaning, optimisation and migration · staging environment for NRCC review · internal QA in parallel.

Phase 3 — Testing, security audit and certification · Weeks 13–20

Functional, responsive, cross-browser, bilingual, accessibility and performance testing · internal VAPT and fixes · **security audit by a CERT-In empanelled agency**, remediation and re-test to clearance · GIGW 3.0 conformance review · **STQC application, shortcoming closure and certification** · UAT with NRCC.

Phase 4 — Hosting, go-live and handover · Weeks 20–24

Production deployment on Govt/MeitY/NIC with DC and DR · SSL installation · DR drill · final content load · go-live on www.nrccamel.res.in · staff training · user and technical manuals · source code, credentials and external-hard-disk backup handed over · ownership certificate and NOC · **warranty and hypercare begin**.

Schedule discipline: the tender caps development at three months from design-template approval and go-live at six months from award, with liquidated damages for delay. Our plan reaches go-live at about week 24 with the certification cycle already absorbed — the single largest schedule risk on engagements of this type, and the reason we start the hosting request and the audit booking in Phase 1 rather than Phase 3.

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672

16 Testing, Training & Handover

Comprehensive testing, staff capability, and an institution that owns what it paid for.

Test coverage

Test type	What we verify
Functional	Every module, form, listing, filter, download and CMS operation against the agreed specification
Bilingual	Language switch on every template, Devanagari rendering, simultaneous publication, language-aware search and metadata
Responsive & cross-browser	Desktop, notebook, tablet and smartphone across Chrome, Edge, Firefox and Safari on Windows, macOS, Android and iOS
Accessibility	Screen reader flow, keyboard operability, contrast, text resize, alt text, form labels and language attributes against GIGW/WCAG
Performance	Click-to-response timing on 3G-class connections, image weight, caching and query behaviour under load
Security	Internal VAPT, then the CERT-In empanelled audit with remediation and re-test
UAT	NRCC administrators run real content tasks on staging and sign off before production cutover

Training of NRCC staff

Role-wise sessions for administrators, editors and unit contributors: creating and publishing bilingual content, uploading documents with metadata, managing menus and themes, using reports, and the archival rules. Sessions are recorded and accompanied by a quick-reference guide, so future staff can be brought up to speed without us.

Handover pack

Complete source code · database schema and dump · design source files · user manual and technical manual · deployment and rollback runbook · credentials register · full backup on external hard disk supplied by us · security audit and STQC certificates · signed NDA, ownership certificate and NOC confirming that design, documents and code are the property of NRCC, with copyright © NRCC on the site.

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE


Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672

17 Warranty & Three-Year Maintenance

One year of free hypercare, then three years of comprehensive maintenance on the quoted price.



What the AMC covers

Area	Included
Corrective	Bug fixing across frontend, CMS and integrations, including defects surfaced by NRCC users
Content	Addition, deletion and updating of pages and documents when NRCC asks us to do it rather than doing it in-house
Adaptive	Design refreshes, new sections, layout changes and occasion themes as institutional needs change
Preventive	Security patching, dependency updates, backup verification, broken-link and missing-Hindi reports, DR drill each year
Certificates	SSL renewal, security re-audit after source-code change, and STQC re-validation arranged by us; third-party fees reimbursed at actuals per the tender
Reporting	Monthly service report — tickets, uptime, analytics summary, security posture and pending items

Service levels we commit to

Situation	Response	Resolution target
Site down, defaced or compromised	Immediate, 24x7	Restoration from verified backup at our cost, with a root-cause note
Security loophole reported	Same day, 24x7	Patch or mitigation, then re-test
Functional defect blocking publication	Within 4 working hours	Next working day, or an agreed workaround
Content upload or update requested	Within 4 working hours	Same working day for routine notices and documents
Minor enhancement or new section	Within 2 working days	Scheduled release with QA and NRCC approval

18 Deliverables, Assumptions & Clarifications

What NRCC owns at the end, and what we need from NRCC to get there.

Deliverables

Three mock-up variants and the approved design	Bilingual website, live on www.nrccamel.res.in
Advanced CMS with role-based access	Migrated and structured existing content
CERT-In security audit clearance	STQC certification and GIGW conformance record
Hosting on Govt/MeitY/NIC with DC and DR	Test reports and UAT sign-off
Staff training and recorded sessions	User manual and technical manual
Source code, credentials and hard-disk backup	NDA, ownership certificate and NOC

Assumptions and clarifications

Item	Our assumption
Content and translation	Text, photographs and Hindi versions are provided by NRCC. We structure, optimise and upload them; professional Hindi translation can be added as a priced option if NRCC prefers.
Hosting allocation	NIC/MeitY allocation is issued in the Institute's name; we configure, deploy and operate it. Any charges levied directly on NRCC by the hosting provider are outside our quoted amount unless stated otherwise in the bid.
Certification bodies	The one-time STQC fee and the CERT-In audit fee are carried by us. Subsequent certifications required for continuous running are arranged by us and reimbursed at actuals against receipt, per clause 18(c).
e-Portal integration	e-Office, e-HRMS, SPARROW, PFMS, CPP, ARMS and Samarth are linked as redirections. Any data-level integration requires the owning agency's API and approval, and would be scoped separately.
Page count	The tender allows pages to increase or decrease. We price a template-driven model; content volume changes do not trigger a change request.
Approval turnaround	Design, content and UAT approvals within five working days each, so the three-month development window and six-month go-live cap hold.
Statutory undertakings	MeitY empanelment evidence, GIGW project experience of the last three financial years, and the non-blacklisting



Item	Our assumption
	undertaking on ₹100 notarised stamp paper are enclosed with the bid.

Why this proposal

The hard part of this tender is not the website — it is landing a CERT-In clearance and an STQC certificate inside six months while migrating a decade of bilingual content, and then standing behind the result for four years. That sequencing is what this proposal is built around: certification treated as a design constraint from the first wireframe, the hosting request raised in week one, and a support commitment that carries restoration liability rather than only a helpdesk number.

We confirm our willingness to attend the pre-bid meeting, to finalise the design as and when required by ICAR–NRCC, Bikaner, and to execute the NDA, ownership certificate and non-blacklisting undertaking on award of work.

For and on behalf of

Source Soft Solutions Private Limited
B-21, CESPL Building, Sector 67, Noida – 201301
Authorised signatory — name, designation, date and seal

Enclosures with the technical bid

MeitY empanelment evidence · GIGW / ICAR project experience of the last three financial years with supporting documents · the design mock-up set · non-blacklisting undertaking on ₹100 notarised stamp paper · NDA draft · company profile and registration documents.

New Jersey, USA – Headquarters

3840 Park Avenue, STE C-205, Edison, NJ 08820
+1 551 358 2076

Dubai, UAE

Unit 107-0140, OF 107, Dubai Investment Park First
+971 50 780 4640

Noida, India

B-21 & B-93, Sector 67, Noida 201301, Uttar Pradesh
+91 98999 41672
